



Old Colony Regional Vocational Technical High School



PMA Consultants



HMFH ARCHITECTS

SCHOOL BUILDING COMMITTEE | 09.16.2024

AGENDA

Name of Board/Committee:	School Building Committee
Date & Time of Meeting:	Monday September 16, <u>2024</u> 6:00 p.m. - Library
Location of Meeting:	Old Colony Regional Vocational Technical High School 476 North Avenue, Rochester, MA 02770
Clerk/Board Member posting notice:	Jolene Costa

Cancelled/Postponed/Revised

(Clerk/Board Member cancelling/postponing/revising meeting)

AGENDA

1. Call to Order
2. Vote to Approve Prior Meeting Minutes
 - o 08/19/24 SBC Meeting Minutes
3. Vote to Approve Invoices
4. Designer Update
 - o Workplan
 - o Educational Programming & Visioning Update
 - o Space Summary Updates
 - o Review Educational and Facilities Goals
 - o Explore Site Options against Goals – VOTE Site Options (if needed)
 - o Review Enrollment Options
 - o Preliminary Design Program (PDP) Submission Review
5. Budget
 - o Updated Concept Level Cost Scenarios (for options comparison ONLY)
 - o Project Funding Options (G.L. c.71 s.16)
6. Schedule/Next Steps
 - o VOTE to Approve Submission of PDP to MSBA
7. New Business
8. Adjournment

PROJECT INVOICES

Old Colony Regional Medical Center

NO PARKING

PERMITS ONLY

INVOICE REGISTER [YEAR-TO-DATE]

Co	Sub	Inv #	Amend #	Month	Invoice Date	Amount	Remaining Billable	MSBA Cost Code	MSBA Cost Code Description
PMA	NA	1	0	Feb-24	March 8, 2024	\$ 2,740.00	\$ 147,930.00	0001-0000	OPM - Feasibility Study
PMA	NA	2	0	Mar-24	April 5, 2024	\$ 4,308.00	\$ 147,930.00	0001-0000	OPM - Feasibility Study
PMA	NA	3	0	Apr-24	May 10, 2024	\$ 3,818.00	\$ 147,930.00	0001-0000	OPM - Feasibility Study
PMA	NA	4	0	May-24	June 6, 2024	\$ 5,468.00	\$ 147,930.00	0001-0000	OPM - Feasibility Study
HMFH	NA	4066	0	Jun-24	July 11, 2024	\$ 43,750.00	\$ 610,850.00	0002-0000	A&E - Feasibility Study
PMA	NA	5	0	Jun-24	July 11, 2024	\$ 2,868.00	\$ 147,930.00	0001-0000	OPM - Feasibility Study
PMA	NA	6	0	Jul-24	August 9, 2024	\$ 2,868.00	\$ 147,930.00	0001-0000	OPM - Feasibility Study
HMFH	NA	4095	0	Jul-24	August 8, 2024	\$ 43,750.00	\$ 610,850.00	0002-0000	A&E - Feasibility Study
HMFH	NA	4044	0	May-24	June 13, 2024	\$ 43,750.00	\$ 610,850.00	0002-0000	A&E - Feasibility Study
HMFH	NA	4133	0	Aug-24	September 12, 2024	\$ 43,750.00	\$ 610,850.00	0002-0000	A&E - Feasibility Study

MSBA OVERVIEW

Old Colony Regional Medical Center

NO PARKING

PERMITS ONLY

MSBA PROCESS

1. Eligibility Period

- Old Colony has submitted a statement of interest and evaluated existing conditions.

3. Feasibility Study

- We help confirm what was found and explored during pre-feasibility.

5. Funding the Project

- We stand by you in securing community/funding approval.

7. Construction

- We oversee the contractor and construction process while keeping a close eye on the quality, budget, schedule, & more.

1

2

3

4

5

6

7

8

2. Forming the Team

- We help you select the Architect that will best meet your project goals.

4. Schematic Design

- We assist in developing a final design program & in negotiating a Project Scope & Budget Agreement.

6. Detailed Design

- Guiding you through design, we also help to generate construction docs, procure bids, & award a construction contract.

8. Completion

- Finalize permits, maximize grant reimbursements, and move students into the school.

DESIGNER UPDATE

Old Colony Regional Medical Center

FREE PARKING

FREE PARKING


PDP WORKPLAN STATUS

PDP Workplan

Old Colony Regional Vocation Technical High School

5/27/2024 HMFH Architects

			2024																											
			May				June				July				August				September				October							
Start	End		6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26	2	9	16	23	30	7	14	21	28		
Preliminary Design Program (PDP)	05/07/24	09/17/24																												
Meetings				*																										
Finalize Contract	05/15/24	05/15/24		*																										
SBC Meetings	TBD	TBD	*				*			*					*					*										
Meeting with Fire and Police	TBD	TBD																		*										
Educational Planning																														
Review/revise existing ed program																														
Visioning Sessions	06/11/24	09/11/24						*										*		*										
Educational Programming																														
Analyze existing schedule / projected growth																														
Meet with Educators	06/10/24	06/10/24						*																						
Populate MSBA Space Template	06/25/24	07/08/24																												
Evaluation of Existing Conditions																														
Walk through of building and systems	05/15/24	05/15/24	*																											
Existing Conditions Drawings Verification																														
Geotechnical investigation																														
Code Review/Structural																														
Haz Mat Analysis																														
Topographic Site Survey																														
Zoning Review																														
Site Development Requirements	06/03/24	07/08/24																												
Site Program Development																														
Water Requirements																														
Orientation/Parking/Traffic																														
Identify Potential Sites																														
Preliminary Evaluation of Alternatives	07/09/24	08/05/24																												
Analysis for Feasibility																														
Preliminary Plan and Site Diagrams																														
Cost implication of Alternatives																														
Community Meetings	TBD	TBD																												
Acushnet																											*			
Carver																										*				
Lakeville																										*				
Mattapoisett																										*				
Rochester																										*				
Submission Preparation & Local Approvals	09/09/24	09/17/24																												
PDP Submission to MSBA	09/17/24	09/17/24																									*			
MSBA Review Period	09/18/24	10/07/24																												
Respond to MSBA Comments	10/8/2024	10/22/2024																												



EDUCATIONAL PROGRAMMING & VISIONING UPDATE

1. **Personalization, Connection, and Ownership**
 - School Identity, Belonging, and Pride
 - Heart of School
 - Showcasing of Student Work
2. **Culture of Learning**
 - Future Focused Education
 - Creative and Fun Learning
 - Success and Engagement
 - Connections to History
3. **Vocational Learning Clusters**
 - With Academic When Feasible
 - Vocational and Academic Connections
4. **School as Community Resource**
 - Promoting Community Connections
 - Schools as Community Service and Hub
5. **Security and Welcome**
 - Ease of Wayfinding
 - Student Safety is Prioritized
6. **Adaptability and Sustainability**
 - Longevity and Efficiency
7. **Indoor/Outdoor Connections**
 - Progressive Learning Spaces
 - Natural Light and Openness
 - Natural Resources
8. **CH 74 Program Equity**
 - Increased Opportunities in Existing Programs for High Demand Areas

SITE APPROACH 1



SITE APPROACH 2



SITE APPROACH 3

COST RANGE
\$242 MILLION - \$285 MILLION
NEW CONSTRUCTION ONLY

PROS

- Maintains fields
- Proper solar orientation can be achieved
- Would work for new construction or addition/renovation
- Allows for development or re-wooding of existing building site

CONS

- Site is close to property line/abutters
- Existing well is un-useable



SITE APPROACH 4












SITE APPROACH 5



SITE OPTIONS 1, 2, & 3



ENROLLMENT COMPARISON – COST

	CH 74 Program Growth	CH 74 Program Additions	NC Total Project Cost Hypothetical District Share	Incremental Cost Increase Hypothetical District Share
560	NO Growth	NO Growth	\$235 Million \$135 Million	
620	ALL Programs right-sized Culinary Program Grows to 68	NO Growth	\$241 Million \$138 Million	+ \$6 Million \$3 Million
728	ALL Programs right-sized Culinary Program Grows to 68 Electrical Program Grows to 60	 	\$269 Million \$153 Million	+ \$28 Million \$15 Million
776	ALL Programs right-sized Culinary Program Grows to 68 Electrical Program Grows to 60	  	\$277 Million \$156.5 Million	+ \$8 Million \$3.5 Million
810	ALL Programs right-sized Culinary Grows to 68 Electrical Program decreases to 54	   	\$285 Million \$163 Million	+ \$8 Million \$6.5 Million

EDUCATIONAL & FACILITY GOALS

Site and Facility Goals, and Objectives		Base Repair	Add Reno - Site Option 1					New Construction - Site Option 3					New Construction - Site Option 2				
		560	560	620	728	776	810	560	620	728	776	810	560	620	728	776	810
FACILITIES GOALS																	
1	Minimize ongoing operational costs (Economic Conservation)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
a	Minimize Building Maintenance Costs	1	2	2	2	2	2	3	3	3	3	3	3	3	3	3	3
b	Minimize Utility Costs	1	2	2	2	2	2	3	3	3	3	3	3	3	3	3	3
c	Minimize Site Maintenance	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3	3
d	Efficient Staffing Operation	1	1	3	2	2	2	1	3	2	2	2	1	3	2	2	2
2	Construction will not disrupt teaching and learning	0	0	0	0	0	0	2	2	2	2	2	3	3	3	3	3
3	Minimize impact on abutters	3	3	3	3	3	3	3	3	3	3	3	1	1	1	1	1
4	Design for Resiliency	1	1	1	1	1	1	3	3	3	3	3	3	3	3	3	3
5	Design for Expansion	1	1	1	1	1	1	3	3	3	3	3	3	3	3	3	3
6	Minimize Disturbance of Existing Fields	3	3	3	3	3	3	3	3	3	3	3	0	0	0	0	0
EDUCATIONAL GOALS																	
1	Vocational Learning Clusters	0	1	1	1	1	1	3	3	3	3	3	3	3	3	3	3
2	Adaptability and Sustainability	1	2	2	2	2	2	3	3	3	3	3	3	3	3	3	3
3	School as a Community Resource	0	1	1	2	3	3	1	1	2	3	3	1	1	2	3	3
4	CH 74 Program Equity	1	1	1	2	3	3	1	1	2	3	3	1	1	2	3	3
5	Indoor/Outdoor Connections	0	2	2	2	2	2	3	3	3	3	3	3	3	3	3	3
6	Security and Welcome	1	2	2	2	2	2	3	3	3	3	3	3	3	3	3	3
7	Personalization, Connection, and Ownership	2	2	2	2	2	2	3	3	3	3	3	3	3	3	3	3
8	Culture of Learning	0	1	1	2	3	3	1	1	2	3	3	1	1	2	3	3
TOTAL		19	28	30	32	35	35	42	44	46	49	49	38	40	42	45	45

PRELIMINARY DESIGN PROGRAM OVERVIEW

3.1.0.1 Table of Contents

3.1.0 PDP Submission

- 1) OPM Certification

3.1.1 Introduction

- 1) Facility Deficiencies
- 2) MSBA Board Action (Invitation to FS)
- 3) Executed Design Enrollment Certification
- 4) Capital Budget Statement Narrative and Target Budget
- 5) Project Directory
- 6) Project Schedule

3.1.2 Educational Program

- 1) Educational Program Narrative

3.1.3 Initial Space Summary

- A. Space Summary for 560 Students
 - B. Space Summary for 620 Students
 - C. Space Summary for 728 Students
 - D. Space Summary for 776 Students
 - E. Space Summary for 810 Students
- A. Existing Floor Plans
- B. Narrative Explaining Any Variances Between Proposed and MSBA Guidelines

3.1.4 Evaluation of Existing Conditions

- 1) Legal Title of Property
- 2) Determination that Property is Available for Development
- 3) Historical Considerations - Project Notification Form
- 4) Site Development Restrictions
- 5) Initial Evaluation of Building Code Compliance for Existing Facility
- 6) Initial Evaluation of MAAB Compliance

- 7) Preliminary Evaluation of Physical Conditions
- 8) Soils Exploration and Geotechnical Evaluation Narrative
- 9) Phase I Environmental Site Assessment Report
- 10) Hazardous Material Identification Study
- 11) Previous Existing Building Studies

3.1.5 Site Development Requirements

- 1) Site Narrative
- 2) Existing Site Plan (Site Survey)

3.1.6 Preliminary Evaluation of Alternatives

- 1) Analysis of School District Capacity & Assignment
- 2) Tuition Agreements
- 3) Rental or Acquisition of Existing Buildings
- 4) Preliminary Evaluations of Alternates Overview
 - 4a) Code Upgrade Option
- 1) Renovation Addition Options
- 2) New Options
- 3) Three Alternatives for PSR

3.1.7 Local Actions and Approvals

- 1) SBC Meetings & Attachments
- 2) Signed Local Actions & Approvals Certification

Appendices

- A. Statement of Interest
- B. MSBA Board Action Letter (Invitation to FS)
- C. Executed Design Enrollment Certification
- D. Visioning Report
- E. Adjacency Diagrams

BUDGET & COST

Old Colony Regional Medical Center

FREE PARKING

FREE PARKING



Building & Site Cost Funding Limit Summary


FY25 \$/sf Building Cost Funding Limit	FY25 \$/sf Site Cost Funding Limit	Estimated 2024-2025 Invitations	Sustainable Level of Invitations
\$550	\$55	18	17
\$569	\$57	16-17	16-17
\$586	\$59	16	16



Project Funding Limit Recommendations

- Adjust the current policy of funding from up to \$550/sf for building costs plus eligible demolition and abatement (exclusive of eligible sitework costs) to **\$586/sf** for building costs plus eligible demolition and abatement (exclusive of eligible sitework costs);
- Apply MSBA’s sitework cost allowance guidelines to include up to **\$59/sf** in addition to the proposed building costs increase of \$586/sf for a total construction cost funding limit of **\$645/sf** plus eligible demolition and abatement; and
- Make the policy effective for districts receiving Board approval of a Project Scope and Budget **on or after January 1, 2025**.

MSBA K-12 MARKET DATA [UPDATED PER 8/28/24 BOARD MTG]

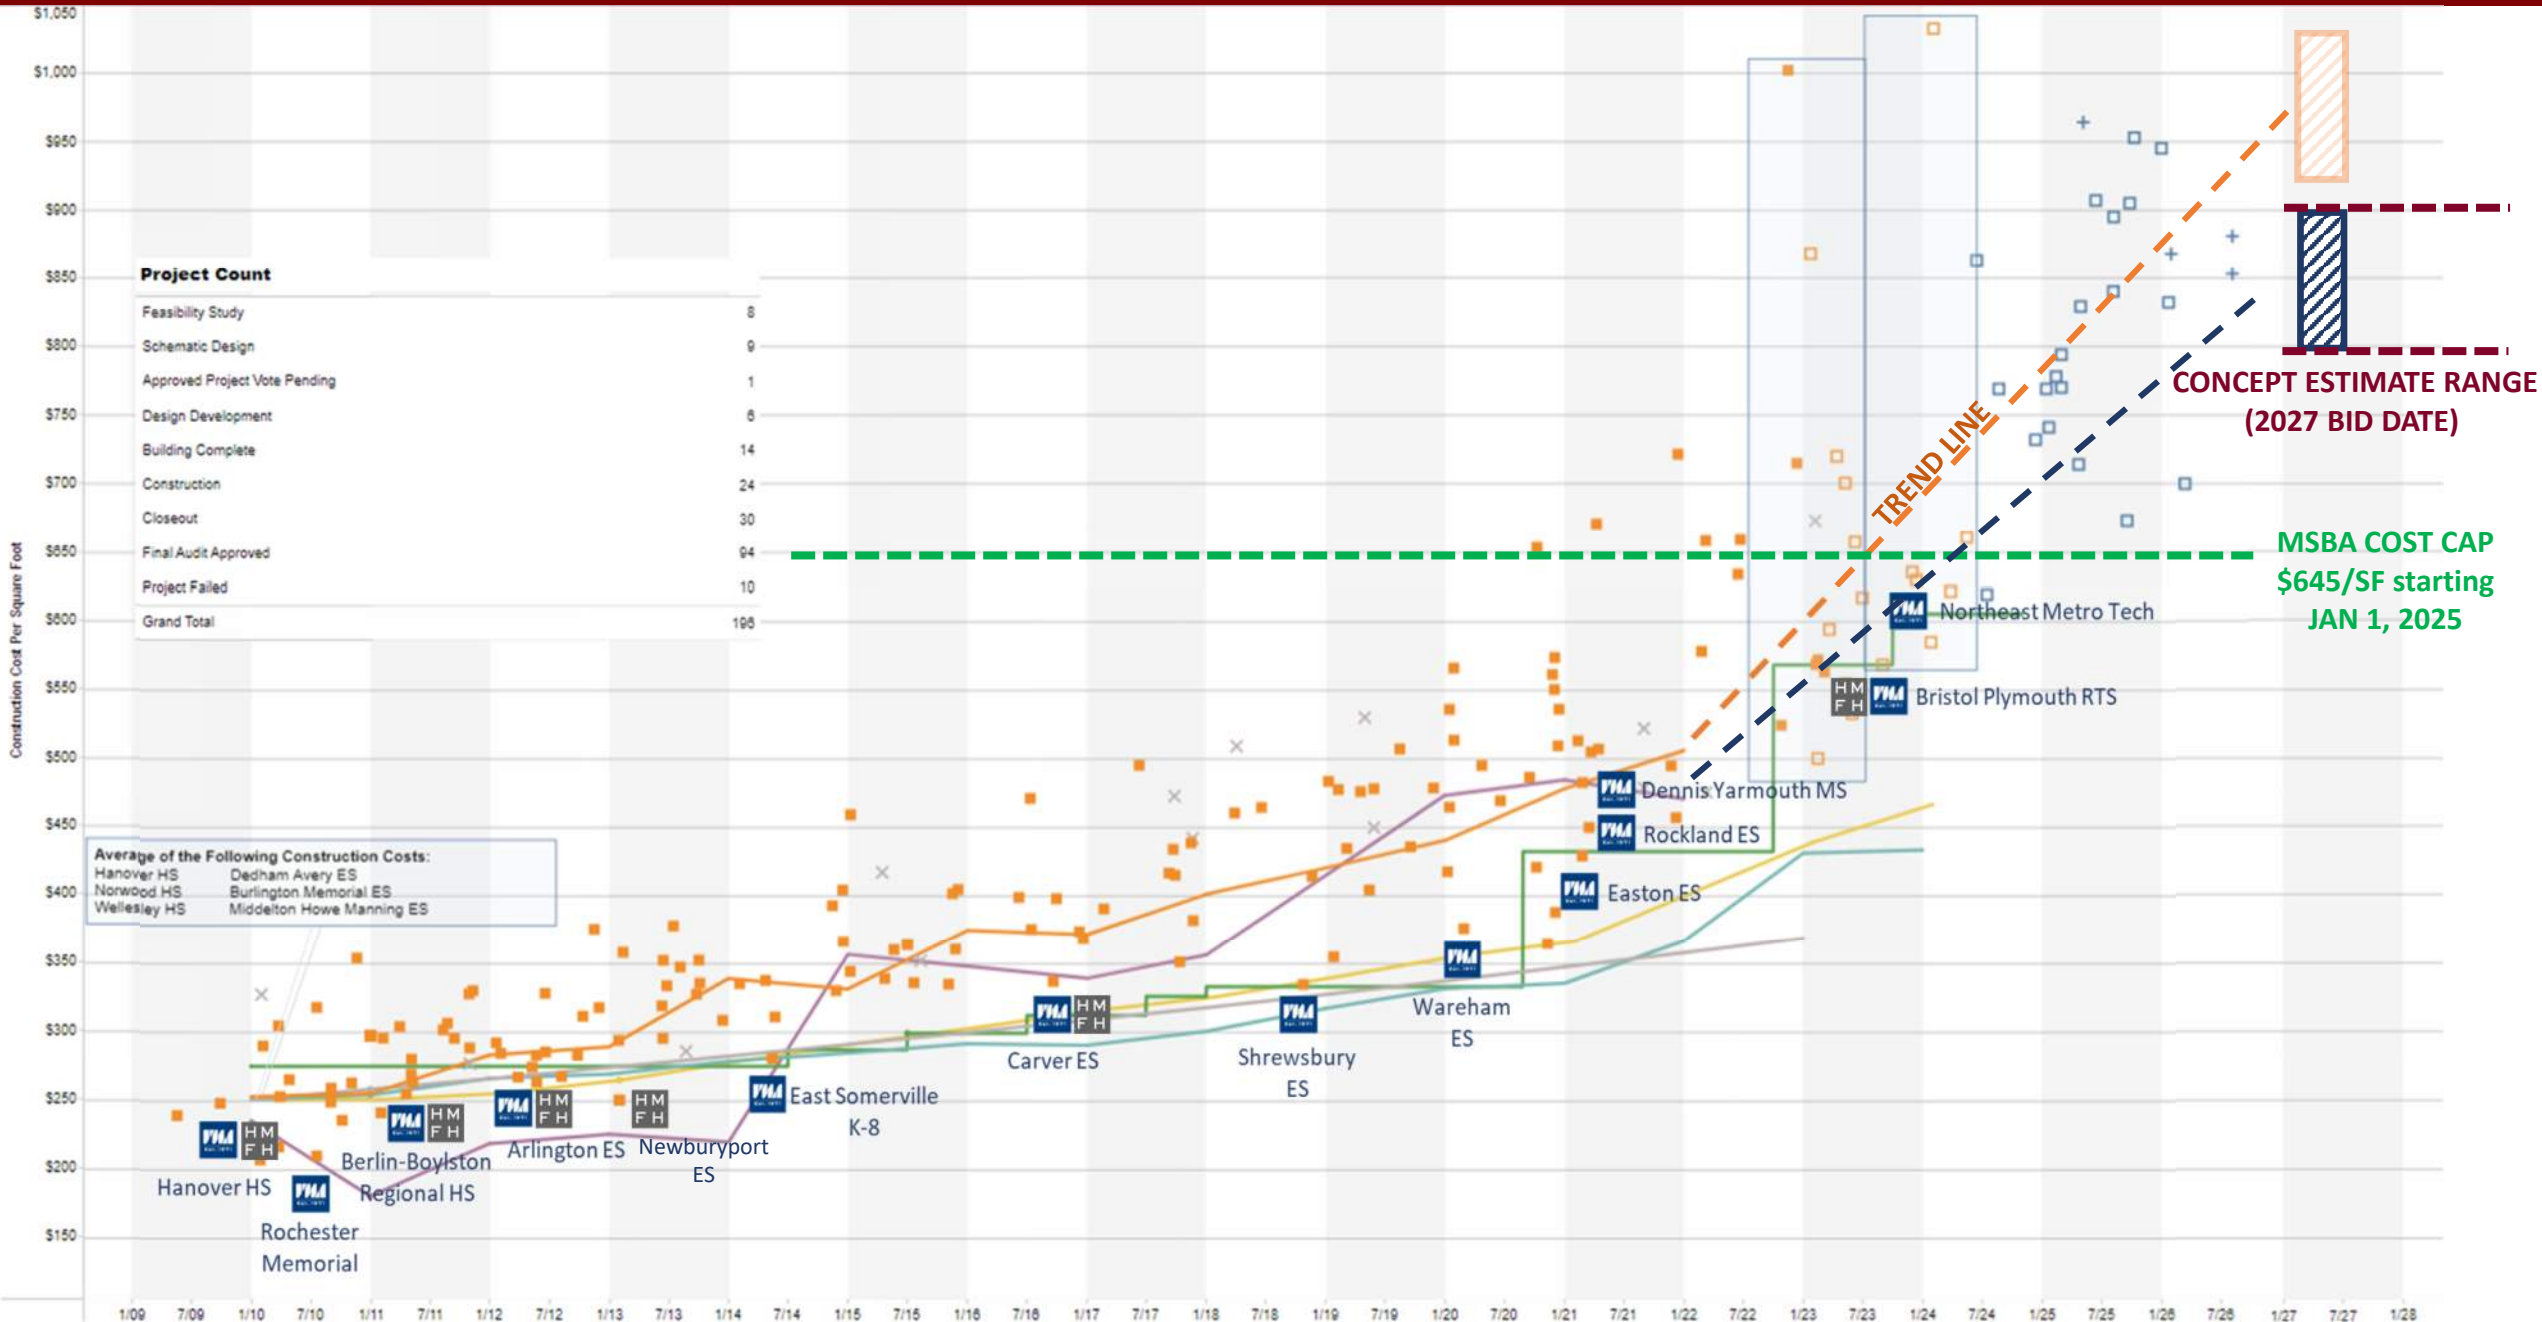


OPTIONS COMPARISON [PM&C CONCEPTUAL LEVEL ESTIMATES]

Hypothetical Project Costs - High Level Cost Scenarios for Options Comparison ONLY

ADDITION-RENOVATION

NEW CONSTRUCTION

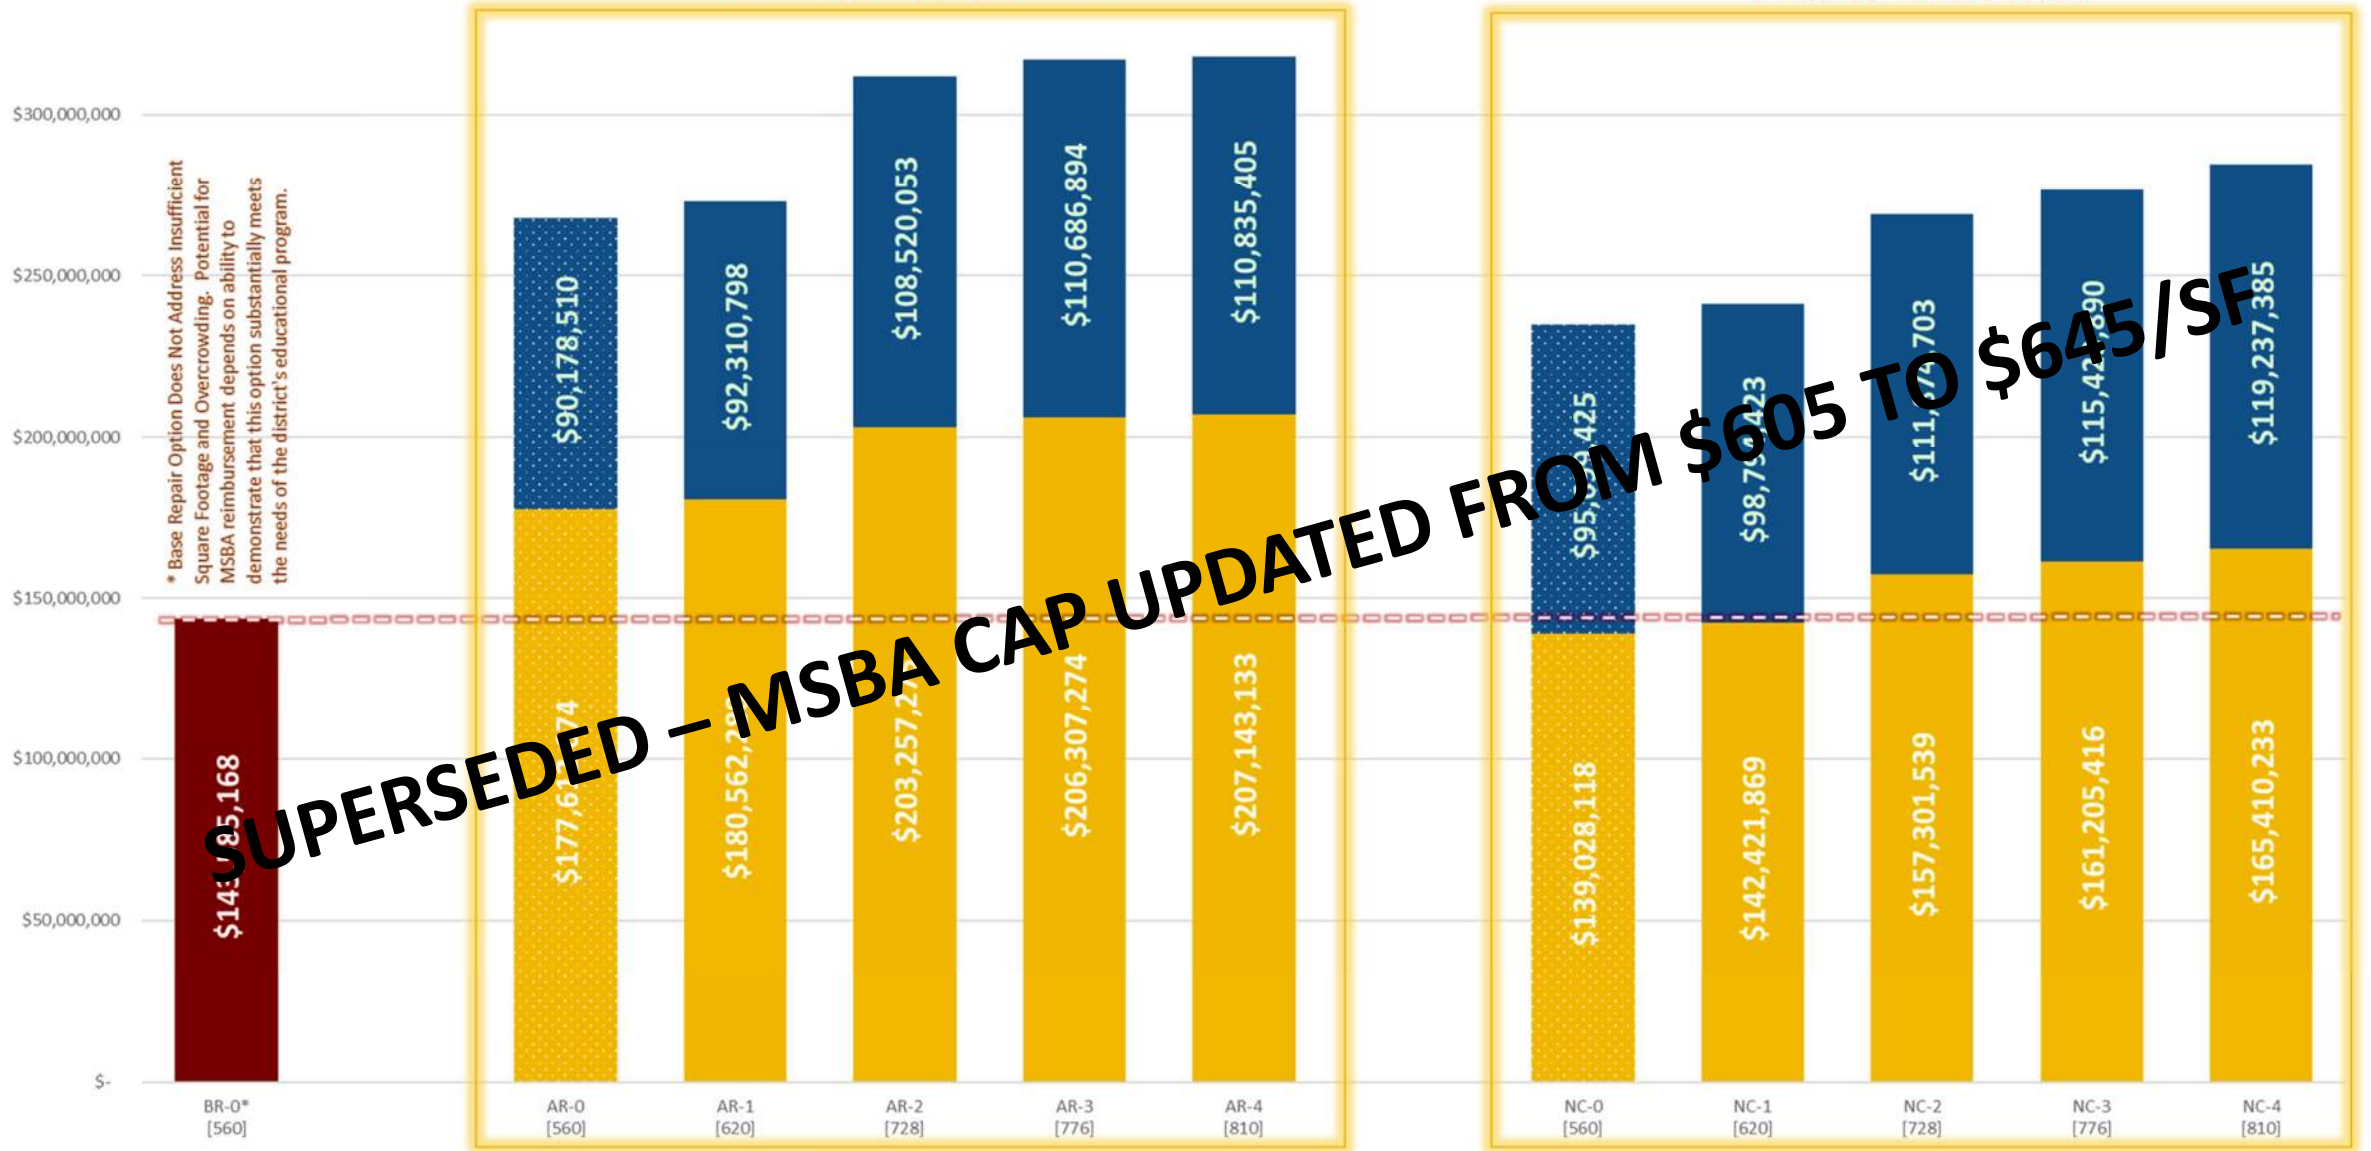

■ HYPOTHETICAL DISTRICT SHARE AMOUNT

■ HYPOTHETICAL MSBA GRANT AMOUNT


SUPERSEDED - MSBA CAP UPDATED FROM \$605 TO \$645/SF

OPTIONS COMPARISON [PM&C CONCEPTUAL LEVEL ESTIMATES]

Hypothetical Project Costs - High Level Cost Scenarios for Options Comparison ONLY

ADDITION-RENOVATION

NEW CONSTRUCTION

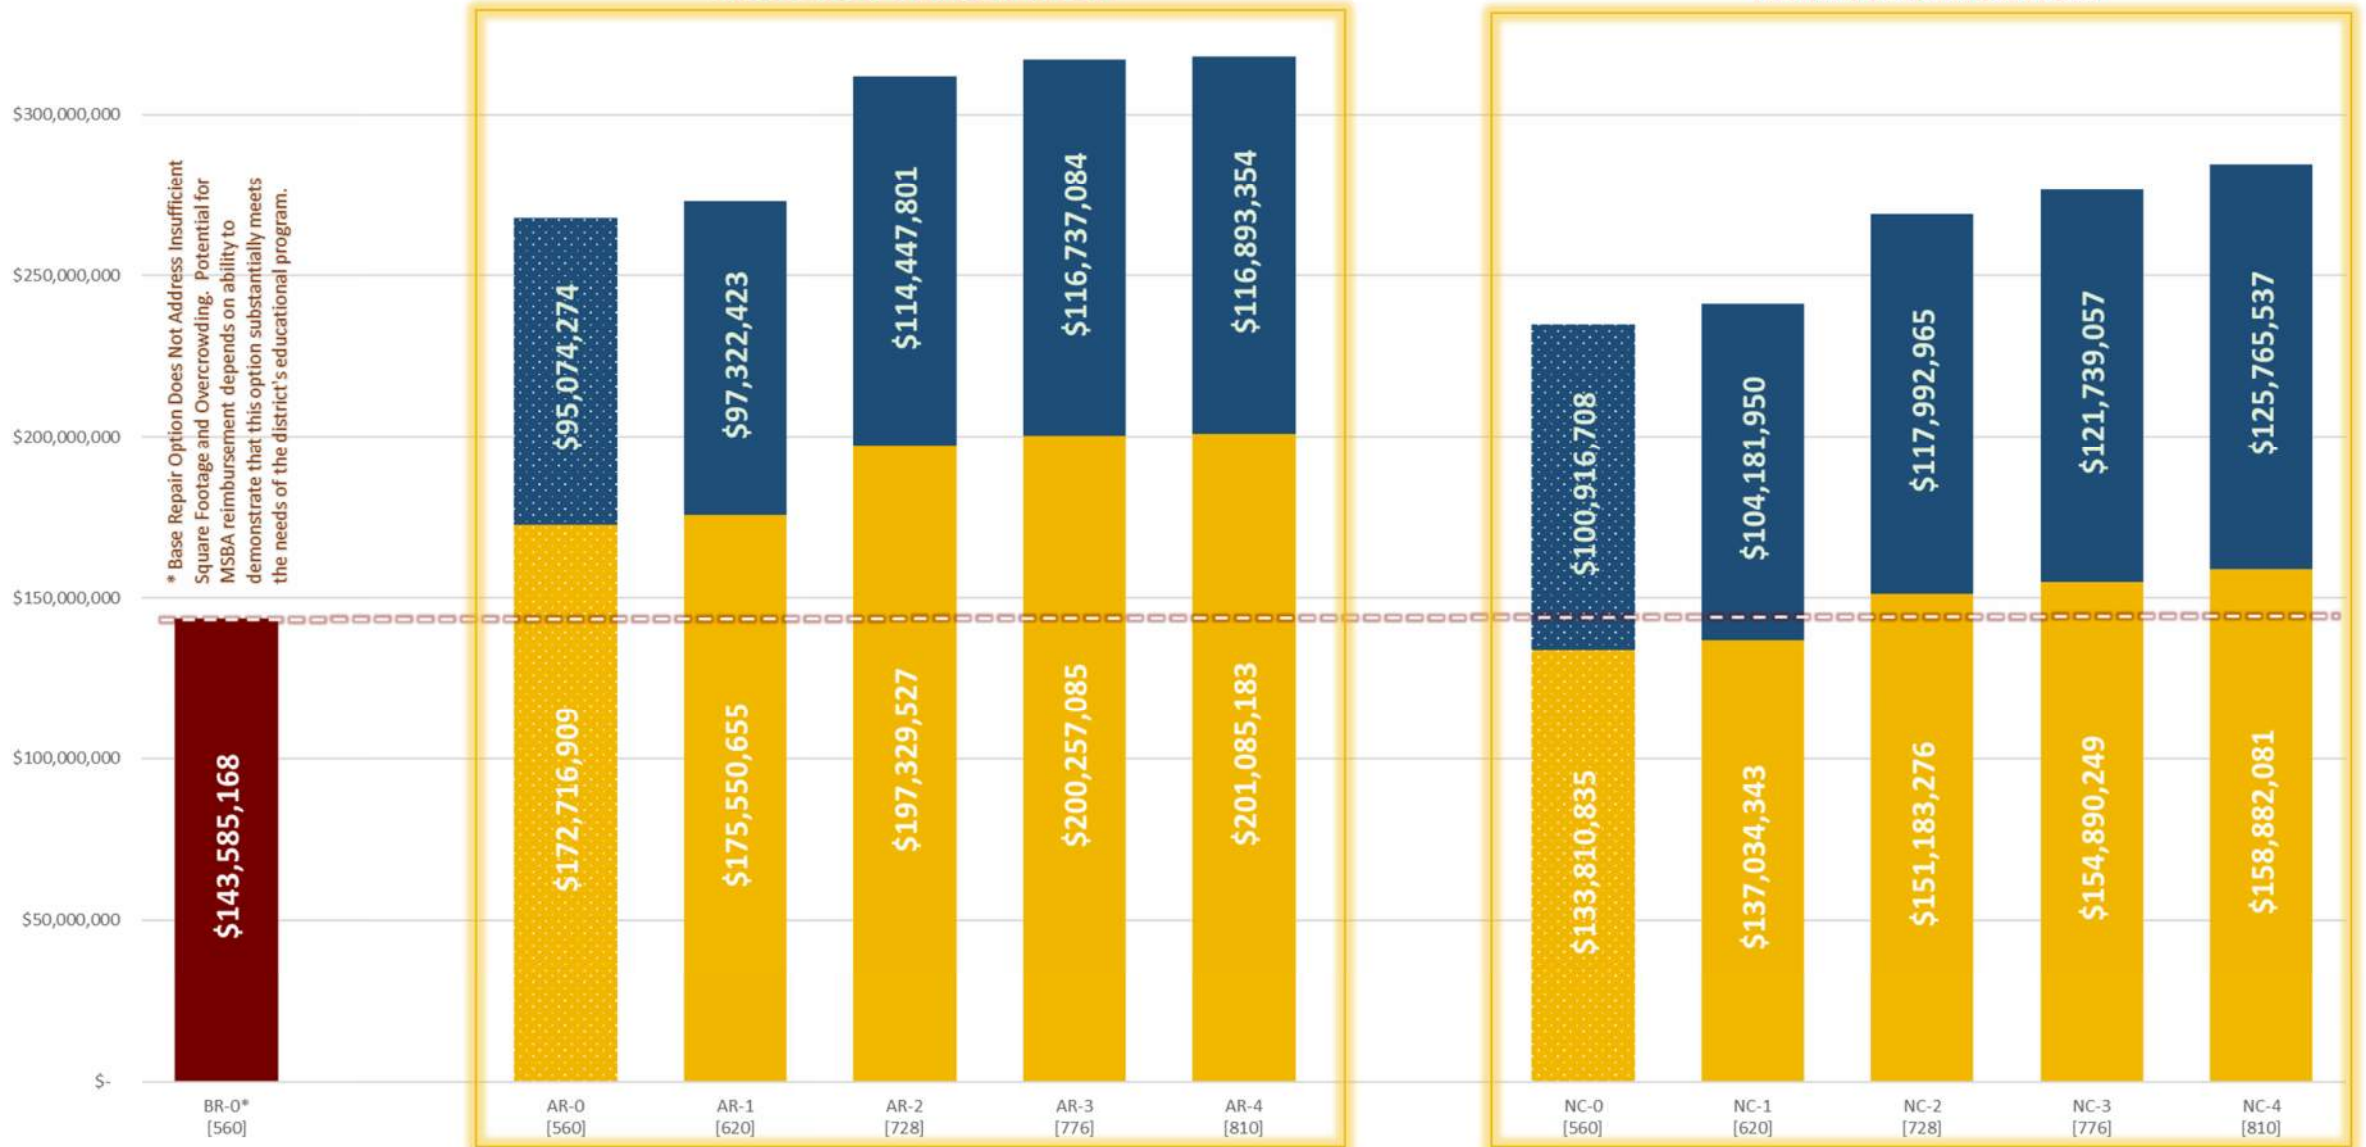

■ HYPOTHETICAL DISTRICT SHARE AMOUNT

■ HYPOTHETICAL MSBA GRANT AMOUNT

LOCAL FUNDING PROCESS

Old Colony Regional Medical Center

FREE PARKING

FREE PARKING

REGIONAL AGREEMENT – PROCESS TO INCUR DEBT

SECTION VII INCURRING OF DEBT

Not later than seven (7) days after the date on which the Committee authorizes the incurring of debt, other than temporary debt in anticipation of revenue to be received from member towns, written notice of the date of said authorization, the sum authorized, and the general purpose or purposes for authorizing such debt shall be given to the Board of Selectmen in each member town.

The Committee may vote to incur debt consistent with the terms and conditions of M.G.L. Chapter 71, Section 16(d) paragraph 1, Section 16(d) paragraph 2, or Section 16(n), as amended. At the time of taking action to incur debt, and except for the incurring of temporary debt in anticipation of revenue, this Agreement authorizes the Committee, by two-thirds (2/3) vote, to select one of the three statutory processes for incurring debt referenced in this Section VII.

APPORTIONMENT OF CAPITAL COSTS/DEBT

C. Apportionment of Capital Costs and Debt

Capital costs shall be apportioned to the member towns annually for the ensuing year in the following manner. Each member town's share of ninety (90) percent of the capital costs for each fiscal year shall be determined by computing the ratio which the town's pupil enrollment in Old Colony Vocational Technical High School on October 1 of the fiscal year preceding the fiscal year for which the apportionment is determined, bears to the total pupil enrollment from all the member towns on the said date. In the event that there is no enrollment in Old Colony Vocational Technical High School from all the member towns on October 1 of any such year, the said ninety (90) percent of capital costs for the ensuing fiscal year shall be apportioned on the basis of the enrollment in all public, private, and parochial schools wherever located of pupils in all the grades from the kindergarten through grade twelve residing in each member town on October 1st. Each member town's share of the other ten (10) percent of the capital costs for each fiscal year shall be apportioned on the basis of the enrollment in all public, private, and parochial schools wherever located of pupils in all grades from kindergarten through grade twelve residing in each member town on said October 1 of the fiscal year preceding the fiscal year for which the apportionment is determined. Capital costs represented by debt service shall be apportioned as a capital cost of the fiscal year in which the debt service falls due.

LOCAL FUNDING PROCESS – 16(D) OPTION

General Law - Part I, Title XII, Chapter 71, Section 16 (malegislature.gov)

(d) To incur debt for the purpose of acquiring land and constructing, reconstructing, adding to and equipping a school building or for the purpose of remodeling and making extraordinary repairs to a school building and for the construction of sewerage systems and sewerage treatment and disposal facilities, or for the purchase or use of such systems with municipalities, and for the purpose of purchasing department equipment; or for the purpose of constructing, reconstructing or making improvements to outdoor playground, athletic or recreational facilities; or for the purpose of constructing, reconstructing or resurfacing roadways and parking lots; or for the purpose of any other public work or improvement of a permanent nature required by the district; or for the purpose of any planning, architectural or engineering costs relating to any of the above purposes; provided, however, that written notice of the amount of the debt and of the general purposes for which it was authorized shall be given to the board of selectmen in each of the towns comprising the district not later than 7 days after the date on which the debt was authorized by the district committee; provided further, that no debt may be incurred until the expiration of 60 days after the date on which the debt was authorized; and provided further, that before the expiration of this period any member town of the regional school district may hold a town meeting for the purpose of expressing disapproval of the amount of debt authorized by the district committee, and if at that meeting a majority of the voters present and voting express disapproval of the amount authorized by the district committee, the debt shall not be incurred and the district school committee shall prepare another proposal which may be the same as any prior proposal and an authorization to incur debt therefor. Debt incurred under this section shall be payable within 30 years, but no such debt shall be issued for a period longer than the maximum useful life of the project being financed as determined in accordance with guidelines established by the director of accounts pursuant to section 38 of chapter 44.

In the case of a vocational regional school district, if the district agreement so provides or is amended to so provide, such debt may also be incurred if two thirds of the member towns do not vote disapproval within said sixty day period provided that said towns which have not voted disapproval agree, within ninety days of the date on which said debt was authorized, to pay the total bond indebtedness authorized by the district committee without contribution by the member towns which voted disapproval of the amount of said debt. The member towns of such vocational regional school district which have voted disapproval of the new indebtedness shall have the right to retain their membership in the school district as provided in their district agreement except that they shall not be allowed any added enrollment that might result solely from the expansion of facilities that occurs on account of said new indebtedness.

LOCAL FUNDING PROCESS – 16(N) OPTION

General Law - Part I, Title XII, Chapter 71, Section 16 (malegislature.gov)

(n) To incur debt for the purposes and terms specified in clause (d); provided that the vote of the district committee authorizing such debt is approved by a majority of the registered voters in the member towns voting on the question at an election called and held pursuant to the following provisions. The election shall be called by a warrant addressed to the registered voters in the member towns and signed by a majority of the members of the district committee which shall set forth the date of the election, the polling place or places in each town, the hours during which the polls are to be open and the question which is to appear upon the ballot. Notice of the election shall be given by posting a copy of the warrant attested by the secretary of the committee in at least one public place in each town and by publishing a copy thereof at least once in a newspaper of general circulation in the district, said posting and publishing to occur at least ten days before said election. A certificate of the secretary shall be conclusive evidence that the warrant was duly posted and published. The number and location of the polling place, or places, in each town shall be determined by the district committee after consultation with the selectmen thereof; and the hours during which all the polls in the district are open shall be uniform throughout the district and shall be not less than four nor more than eight consecutive hours. The district committee shall be responsible for preparing the ballots used at the election. The town clerk of each town shall certify the results of the election to the district committee. Except as provided herein the election shall be conducted in each town in the same manner as town meetings for the election of town officers. The expenses of the election shall be paid by the regional school district as an operating expense of the district; and if provision for their payment is not included in the budget for the year in which they are incurred, the district committee may use any available funds of the district or may transfer the sums required from appropriations included in the budget. The defeat of a proposal for incurring debt shall not prevent the resubmission of the same proposal as a new authorization.

LOCAL FUNDING OPTIONS - SUMMARY

IF G.L. c71 s16(d):

- Motion & vote by School Committee.
- Notice issued to member communities within 7 days.
- Member communities have 60 days to express disapproval via majority vote at Town Meeting (or City Council), if any community disapproves then debt shall not be incurred.
- Debt exclusion still requires vote in each community where applicable.

IF G.L. c71 s16(n):

- Identify special election date (35-day minimum notice required).
- Motion & vote by School Committee.
- Election warrant issued to registered voters minimum 10 days prior to election.
- One polling location in each community, open 4-8 hours. District responsible for election costs.
- Results from all member communities combined, majority vote prevails.
- Debt exclusion still requires vote in each community where applicable.


SCHEDULE & NEXT STEPS

Old Colony Regional Medical Center

FREE PARKING

FREE PARKING

PROJECT TIMELINE

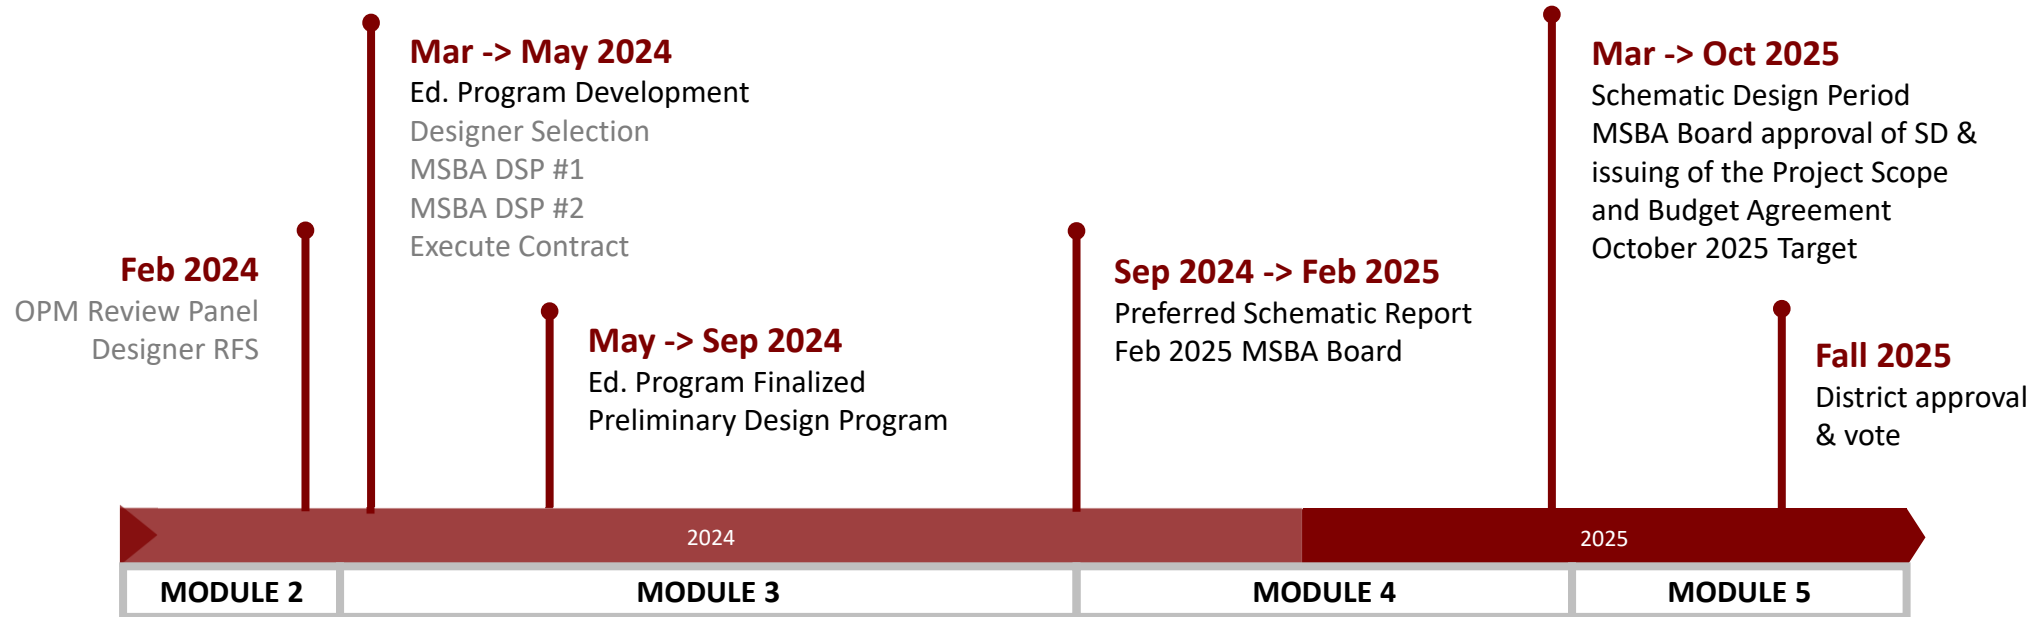



**YOU ARE
HERE**

TIMELINE KEY

Dates are Forecast based on an estimated MSBA Board Meeting schedule

PROJECT SCHEDULE

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Preliminary Design Program					
A1110	School Dept Update Education Program	50	02-Jan-24 A	11-Mar-24 A	
A1470	Visioning Session #1	1	11-Jun-24 A	11-Jun-24 A	
A1130	Evaluation of Existing Conditions	30	21-May-24 A	01-Jul-24 A	
A1120	Draft Initial Space Summary	10	08-Jul-24 A	19-Jul-24 A	
A1140	Establish Site Development Requirements	5	08-Jul-24 A	19-Jul-24 A	
A1150	Preliminary Evaluation of Alternatives	20	22-Jul-24 A	16-Aug-24 A	
A2720	Visioning Session #2	1	27-Aug-24 A	27-Aug-24 A	
A1210	Cost & Schedule Analysis of PDP Alternatives	13	19-Aug-24 A	04-Sep-24 A	
A1190	Education Program Refined with Designer Input	20	21-May-24 A	11-Sep-24 A	
A1200	Final Review & Acceptance of Education Program	10	29-Aug-24 A	11-Sep-24 A	
A2730	Visioning Session #3	1	11-Sep-24 A	11-Sep-24 A	
A1220	SBC Approval of PDP Alternatives	5	05-Sep-24 A	16-Sep-24 A	
A1160	Compile & Submit PDP to MSBA (9/17)	4	12-Sep-24 A	17-Sep-24 A	
A1170	MSBA Review Period	21	18-Sep-24 A	08-Oct-24	21
A1180	Respond to MSBA Review Comments	14	09-Oct-24	22-Oct-24	21
Preferred Schematic Report					
A1230	Evaluation of Existing Conditions (Phase II Exploration)	30	18-Sep-24	29-Oct-24	0
A1240	Final Evaluation of Alternatives	13	25-Oct-24	12-Nov-24	0
A1250	Identification and Development of Preferred Solution	15	13-Nov-24	03-Dec-24	0
A1260	Local Actions and Approvals	5	04-Dec-24	10-Dec-24	0
A1310	Compile and Submit PSR [12/13/2024 Deadline]	3	11-Dec-24	13-Dec-24*	0
A1280	MSBA PSR Review Period	21	14-Dec-24	03-Jan-25	39
A1300	Response to MSBA PSR Review Comments Due	14	04-Jan-25	17-Jan-25	39
A1290	MSBA Facilities Assessment Subcommittee [1/15/24 or 1/29/24]	1	29-Jan-25	29-Jan-25*	0
A1270	MSBA Board of Directors Approval of PSR [2/26/24]	0		26-Feb-25*	0

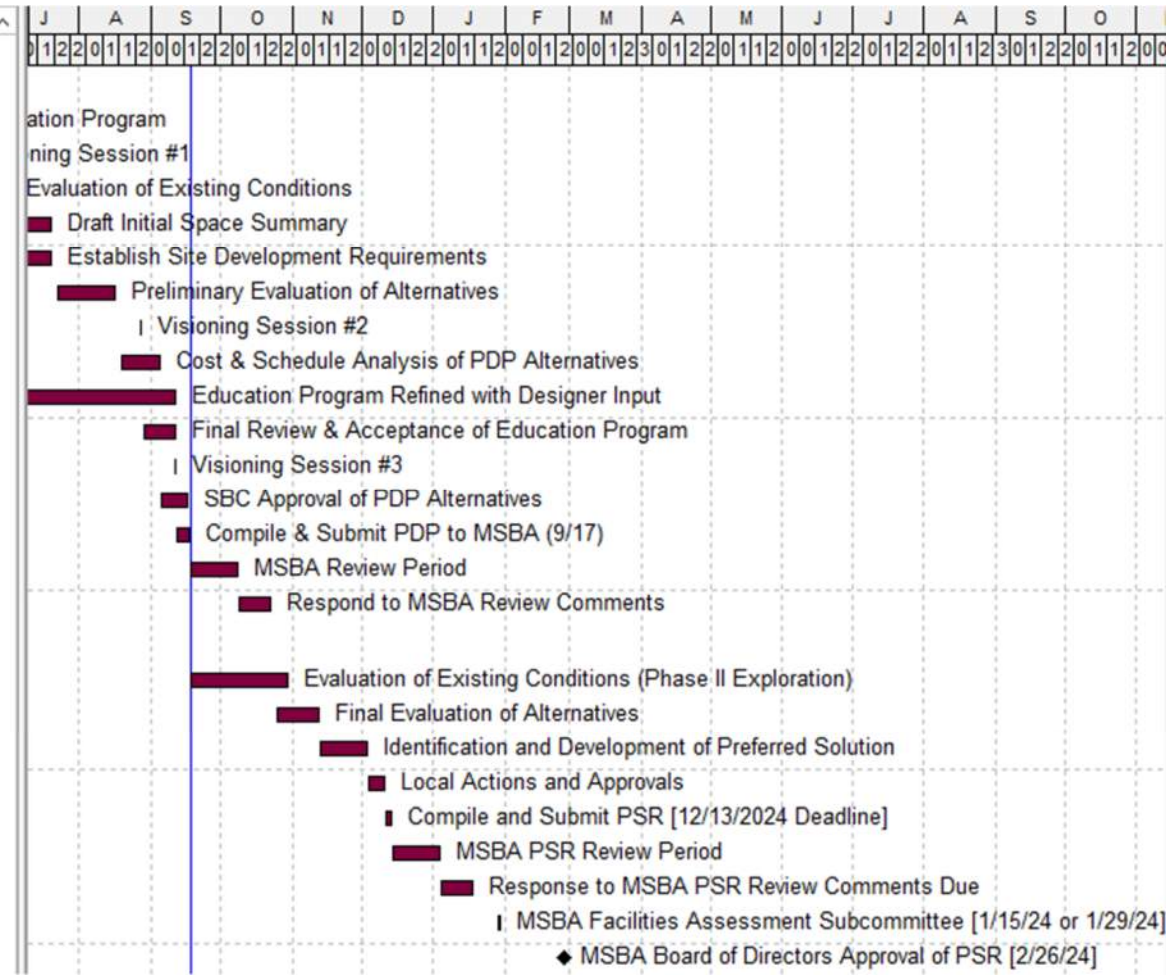

KEY DATES

- School Building Committee: Tuesday 5/7 6:00PM Since Last SBC
- School Committee Introduction: Wednesday 5/15 6:30PM
- Day w/ Faculty(User Group Mtgs): Monday 6/10 7:30AM-3:00PM
- Educational Visioning Session #1: Tuesday 6/11 12:00PM-3:00PM
- School Building Committee: Thursday 6/13 6:00PM
- School Building Committee: Monday 7/8 6:00PM
- School Building Committee: Monday 8/19 6:00PM
- Educational Visioning Session #2: Tuesday 8/27 11:45AM-2:15PM
- Educational Visioning Session #3: Wednesday 9/11 11:45AM-2:15PM

- School Building Committee: Monday 9/16 6:00PM **Upcoming**
- Preliminary Design Program: Tuesday 9/17, 2024
- School Building Committee: Monday 10/21, 6:00PM
- Preferred Schematic Report: Friday 12/13, 6:00PM

VOTE

**TO APPROVE SUBMISSION OF
PRELIMINARY DESIGN PROGRAM TO MSBA**

NEW BUSINESS

Old Colony Regional Medical Center

FREE PARKING

FREE PARKING



PMA Consultants



HMFH ARCHITECTS

OldColony@PMAConsultants.com **QUESTIONS? | THANK YOU!**
